


Date: 5/4/2016 Author: CentraCom Project: Best Western Mtn View Inn Springville

Comments:

Installing 3 handholes. Installing 1 1/4" conduit/fiber for 875' on South side of SR 75. Directional drill, no asphalt cut required.

Taper, Buffer Zone & Sign Spacing				
Posted speed	Mini Taper Length	Length of Buffer	Min Sign Spacing	Devices Spacing
30	180'	200'	100'	15'
35	245'	250'	350'	20'
40	320'	305'	350'	27'
45	340'	380'	500'	45'
50	600'	425'	500'	50'
55	660'	495'	500'	55'
60	720'	570'	500'	60'
65	780'	645'	500'	65'

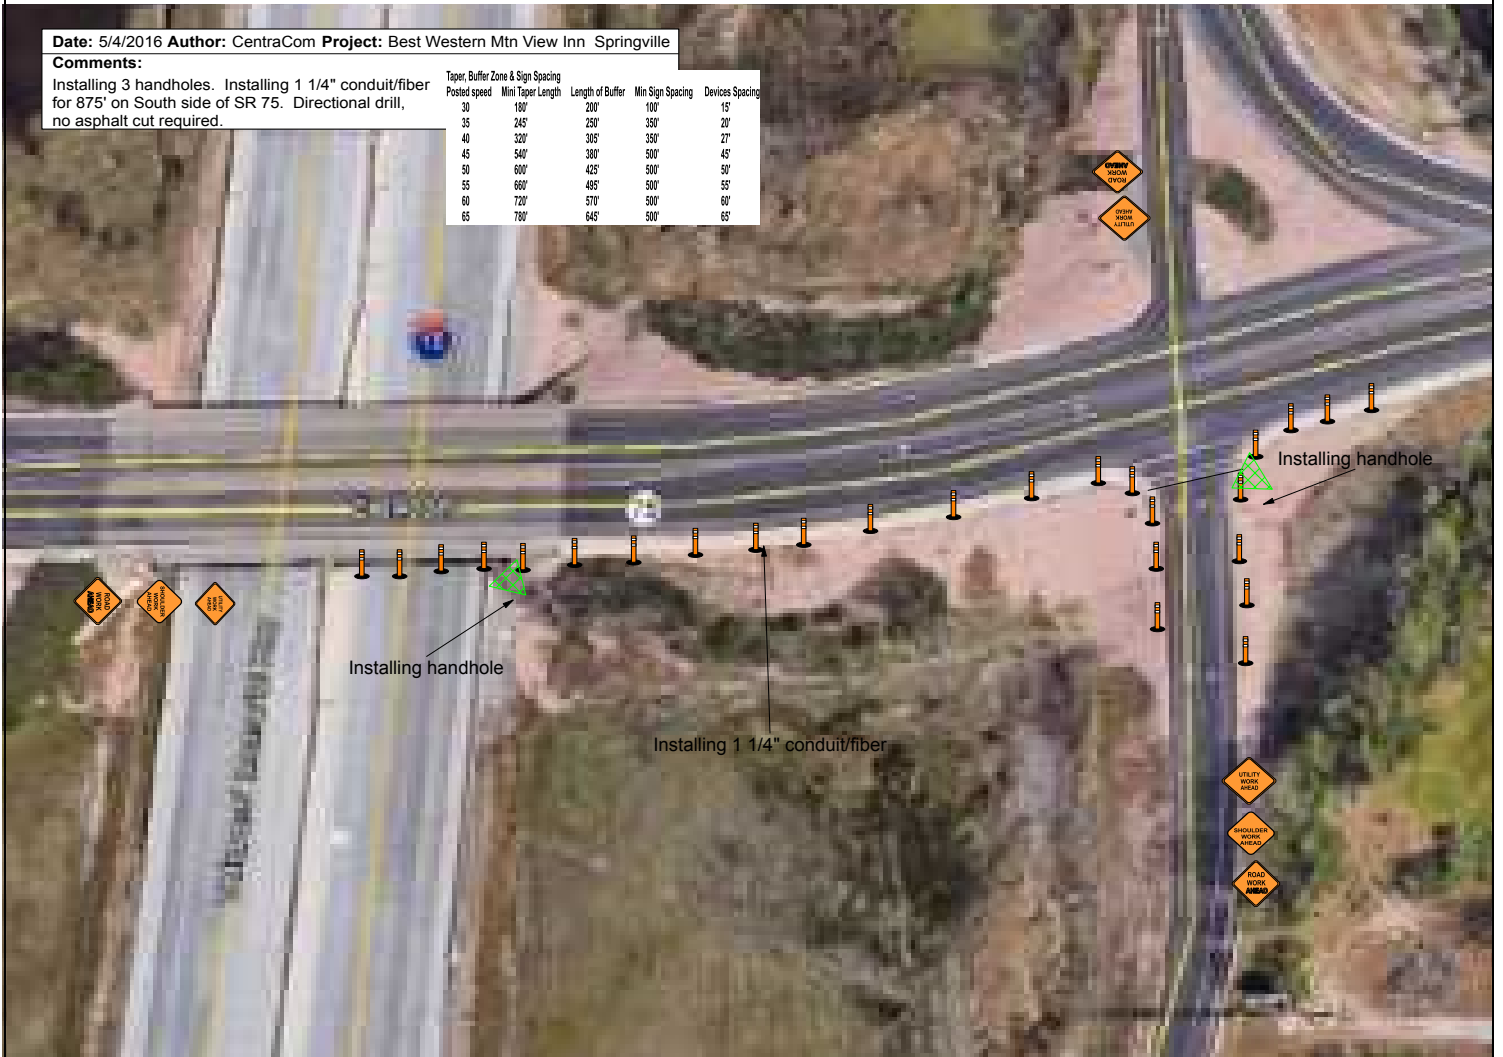

Installing handhole

Installing 1 1/4" conduit/fiber

Installing handhole
