


Date: 6/9/2016 **Author:** CentraCom **Project:** Questart Mona Monitoring Station
Comments:
Installing 450' 1 1/4" conduit/fiber and handhole.

Taper, Buffer Zone & Sign Spacing				
Posted speed	Mini Taper Length	Length of Buffer	Min Sign Spacing	Devices Spacing
30	180'	200'	100'	15'
35	245'	250'	350'	20'
40	320'	305'	350'	27'
45	540'	380'	500'	45'
50	600'	425'	500'	50'
55	660'	495'	500'	55'
60	720'	570'	500'	60'
65	780'	645'	500'	65'

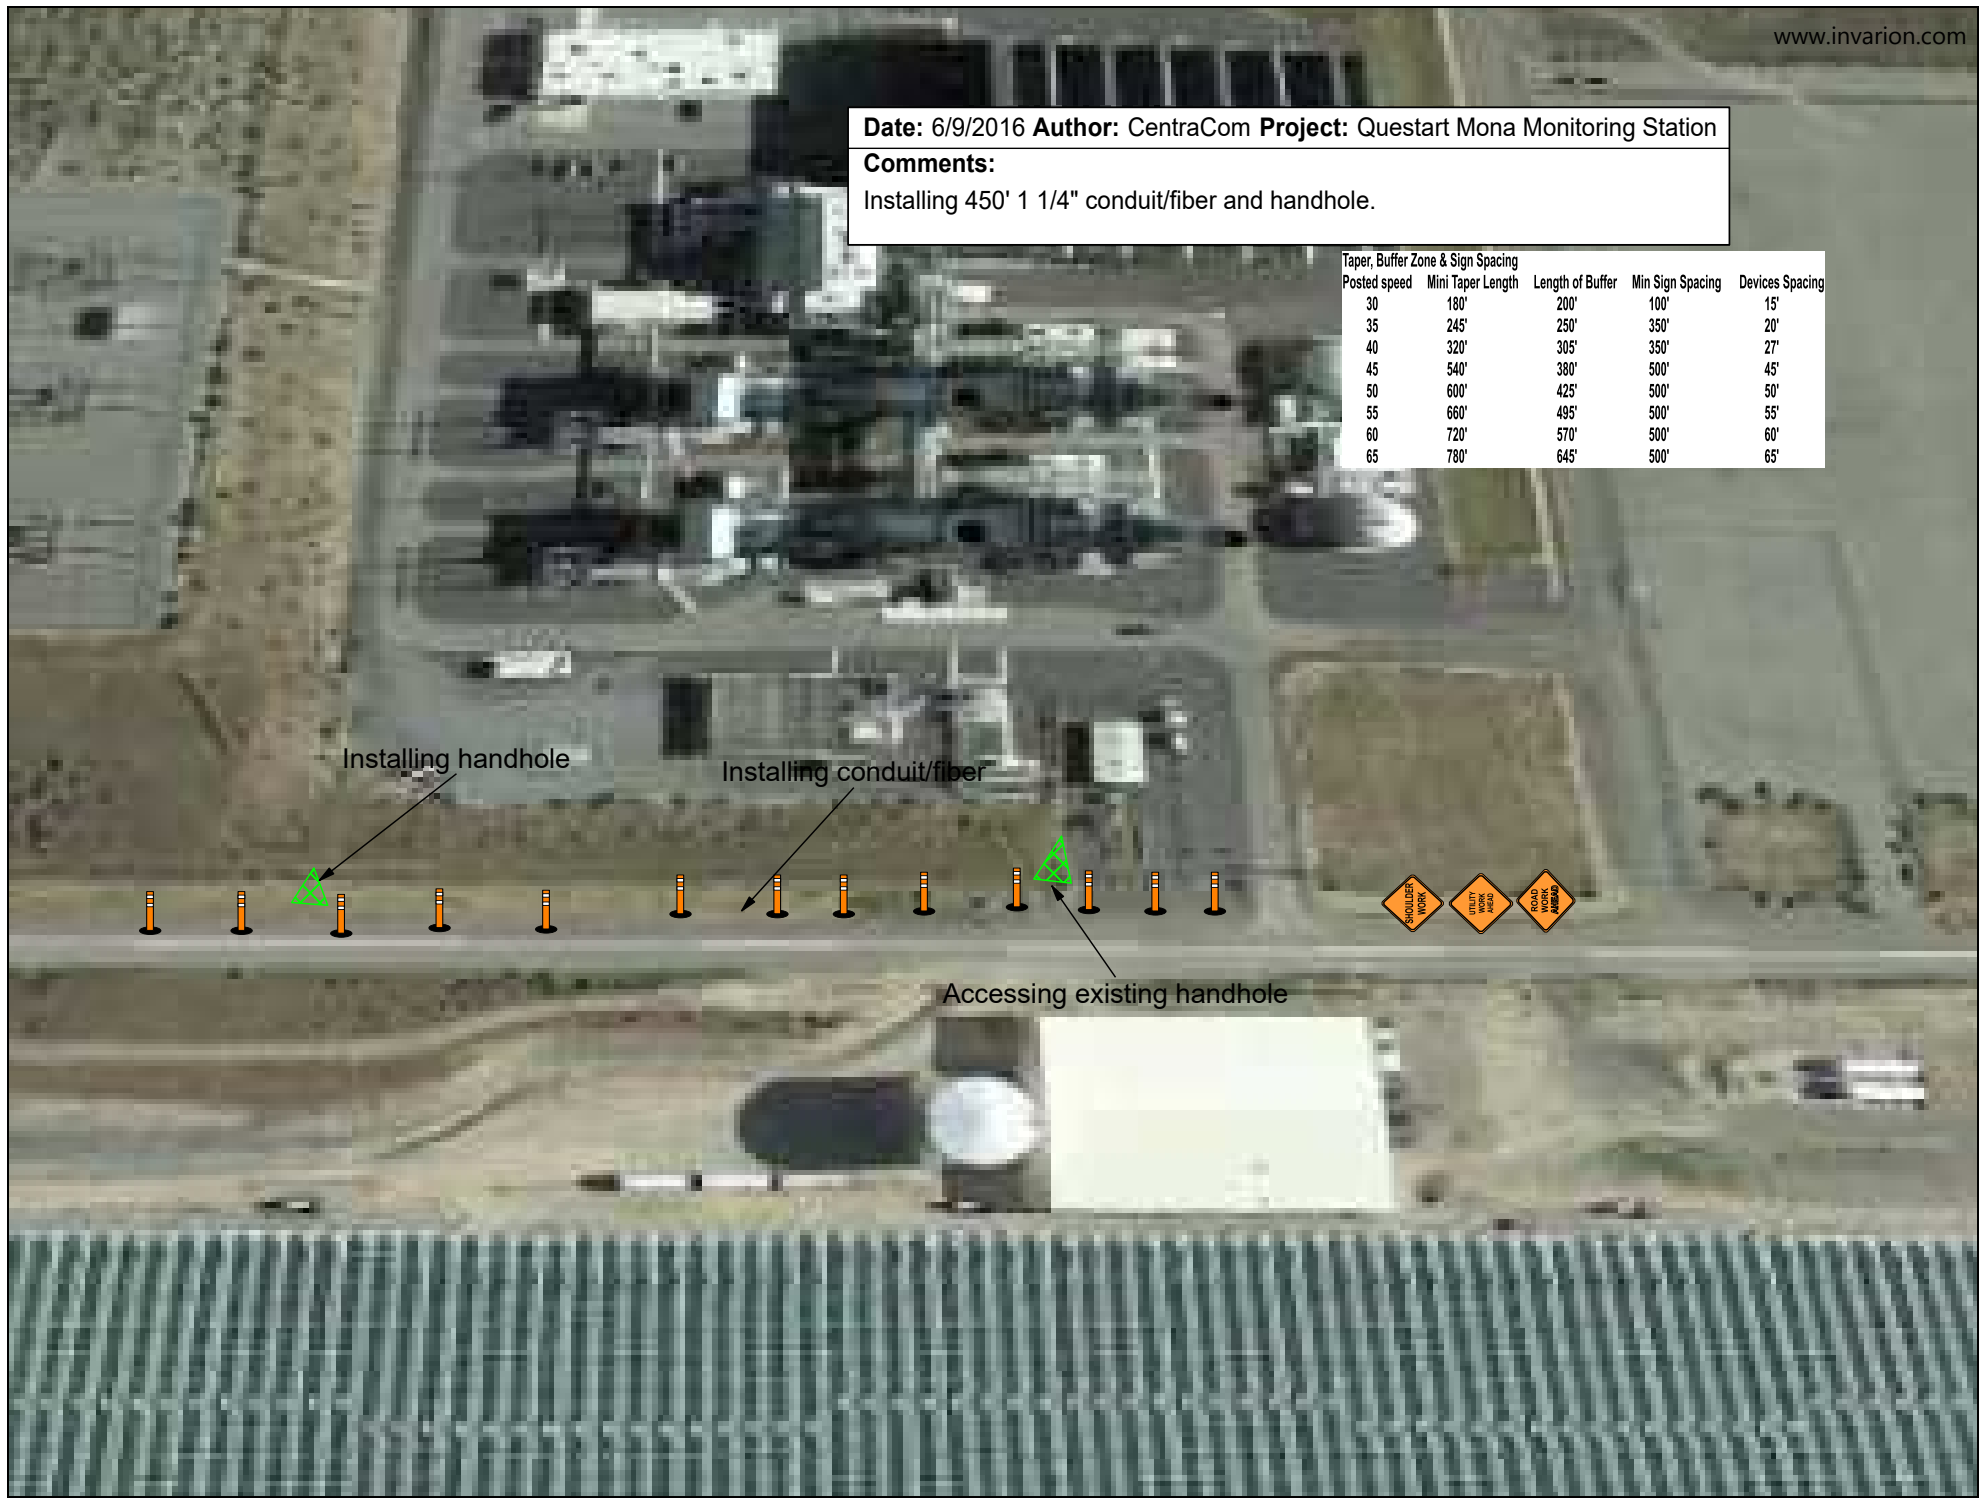

Installing handhole

Installing conduit/fiber

Accessing existing handhole

