


Date: 11/14/2017 Author: CentraCom Project: InMoment South Jordan

Comments:
 Installing 1 1/4" conduit/fiber. Directional
 drill road crossing. Installing handholes.
 Conduit/fiber 10" back of sidewalk.

Posted speed	Mini Taper Length	Length of Buffer	Min Sign Spacing	Devices Spacing
30	180'	200'	100'	15'
35	245'	250'	350'	20'
40	320'	305'	350'	27'
45	540'	380'	500'	45'
50	600'	425'	500'	50'
55	660'	495'	500'	55'
60	720'	570'	500'	60'
65	780'	645'	500'	65'

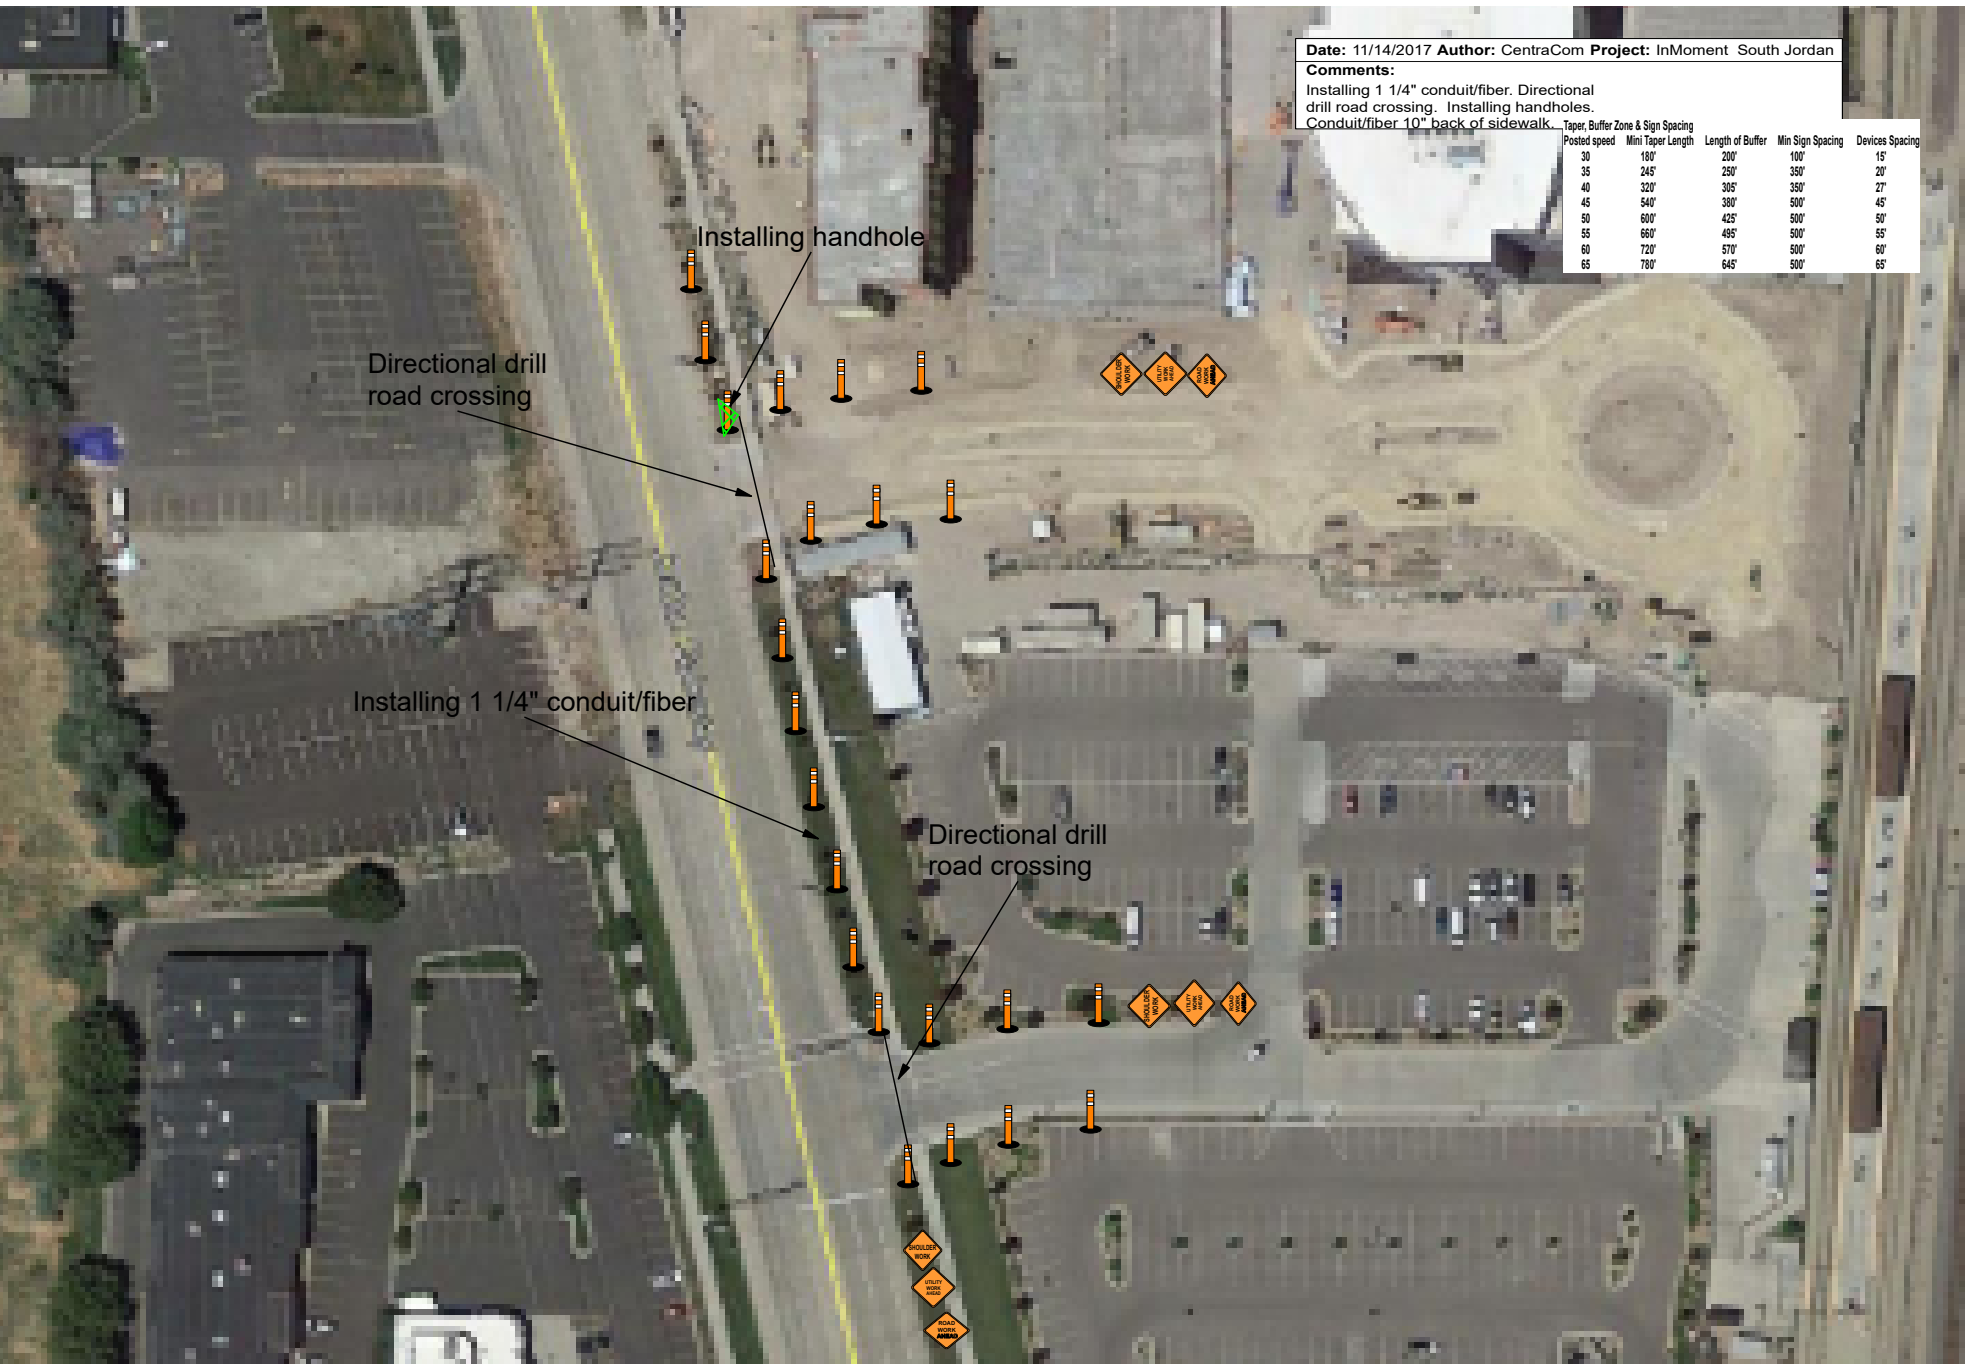

Installing handhole

Directional drill road crossing

Installing 1 1/4" conduit/fiber

Directional drill road crossing
